

## Garretson Elementary 2017-2018 Phase 2

### Weekly Construction Progress Update, Week Ending November 9, 2018

Billing through 10/31/18 reflects that the project is 99% Contract completion date: November 2018

#### This week's activities

- Installed rolling book shelves at Media Center.
- Installation of roller shades/ blinds at Media Center
- Installation of room signage on Building C
- Complete grading & landscape at south end of school.

#### Next week's activities


- Final clean up in Building C
- Installation of ornamental fencing around site
- Continued working on punch list items.



**Media Center, Rolling shelves**



**Media Center, Blinds**

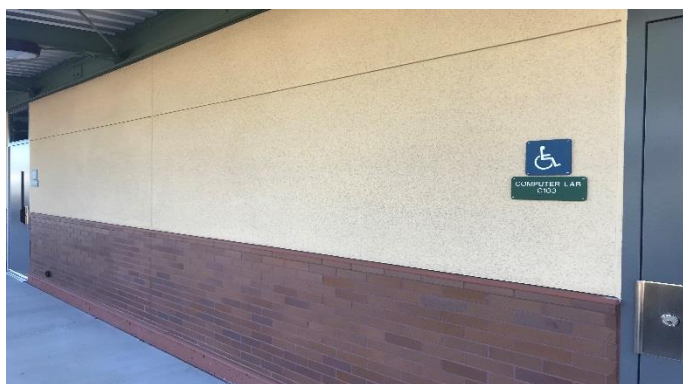

**Building C, Room signage**



**South end, Landscaping**
