

## Garretson Elementary 2017-2018 Phase 2

### Weekly Construction Progress Update, Week Ending September 7<sup>th</sup>, 2018

Billing through 8/31/18 reflects that the project is 94% Contract completion date: October 2018

#### This week's activities


- Building D casework install
- Exterior painting in progress building C & D
- Finishing T-Bar building D
- Taping continues Building C

#### Next week's activities

- Finish painting at Building D Exterior
- Start T-Bar building C
- Finish taping drywall building C
- Building C & D sheetmetal starting



Building C exterior painting

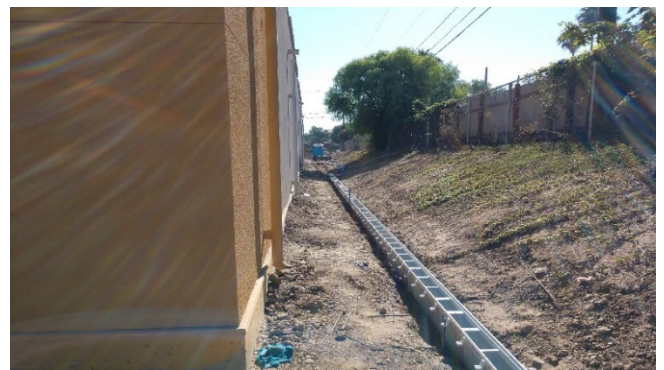

Trench drain South side building D



Casework in progress at building D



Building D Door Installation
