

## Garretson Elementary 2017-2018 Phase 2

### Weekly Construction Progress Update, Week Ending September 14, 2018


Billing through 8/31/18 reflects that the project is 94% Contract completion date: October 2018

#### This week's activities

- Continue Casework in Building D
- Light fixtures installed in Building D
- Finish T-Bar / Dropping tiles
- Start painting in Building C

#### Next week's activities

- Finish T-Bar in Typical rooms Building C
- Grade for site concrete and Start form work
- Power up Building D

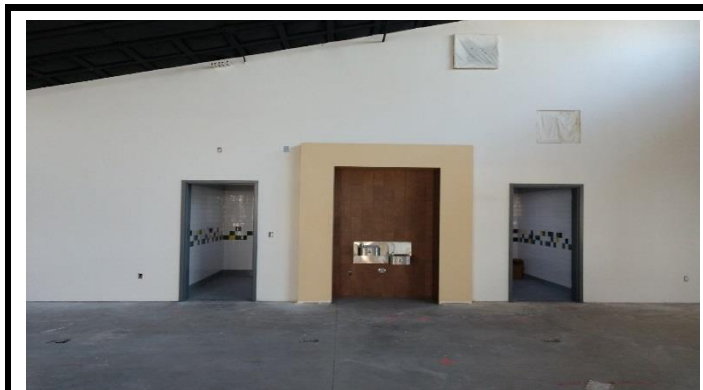


**Building C, Paint complete**



**Building C, Paint complete**



**Building D, Casework in Progress**

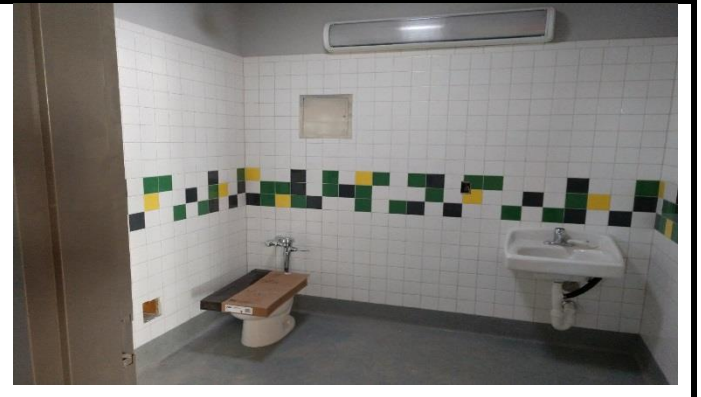

**Building D Restroom Finishes in Progress**
